



**ORRS BRIDGE (CUMBERLAND COUNTY BRIDGE # C-2),
OVER THE CONODOGUINET CREEK
HAMPDEN TOWNSHIP, CUMBERLAND COUNTY, PENNSYLVANIA**

July 10th, 2019

Report # 7

CONSTRUCTION SCHEDULE

- Bid Opening: November 1, 2018 (Complete)
- Pre-Construction Utility Relocations: December 2018 to May 2019 (Complete)
- Construction*:
 - Phase 1 Bridge Construction: July 2019 to March 2020
 - Phase 2 Roadway Approach Construction: March 2020 to April 2020
 - Phase 3 Bridge Demolition: April 2020 to October 2020


** Contingent on timely utility relocations, weather, and stream conditions*

UPCOMING ACTIVITIES

- Completion of site clearing (see progress photos below)
- Stream relocation
- Installation of temporary cofferdam
- Installation of temporary causeway
- Drill holes for sheet piling in preparation for waterline installation



Site Clearing (Looking South)

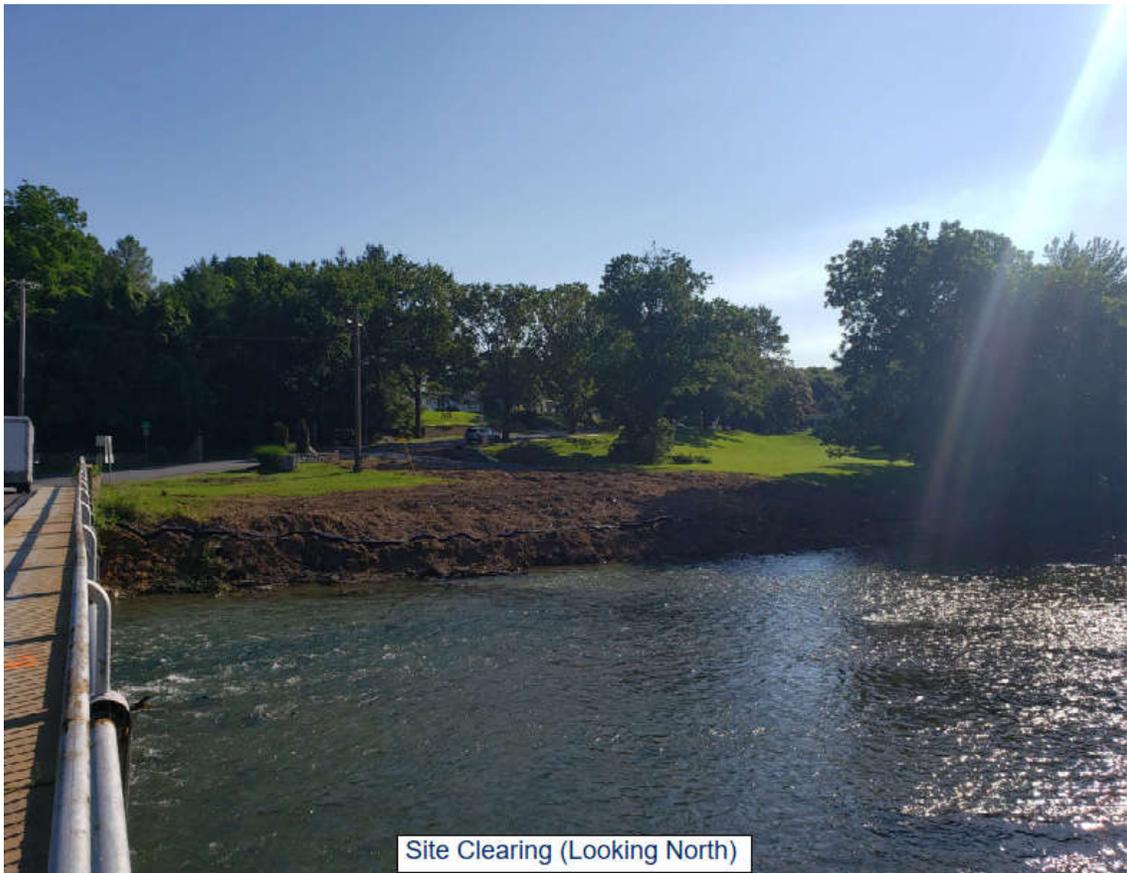

Site Clearing (Looking North)
