


TRAFFIC STAGING PLAN


(CONTINGENT UPON CONTRACTOR'S MEANS & METHODS)

STATION 5

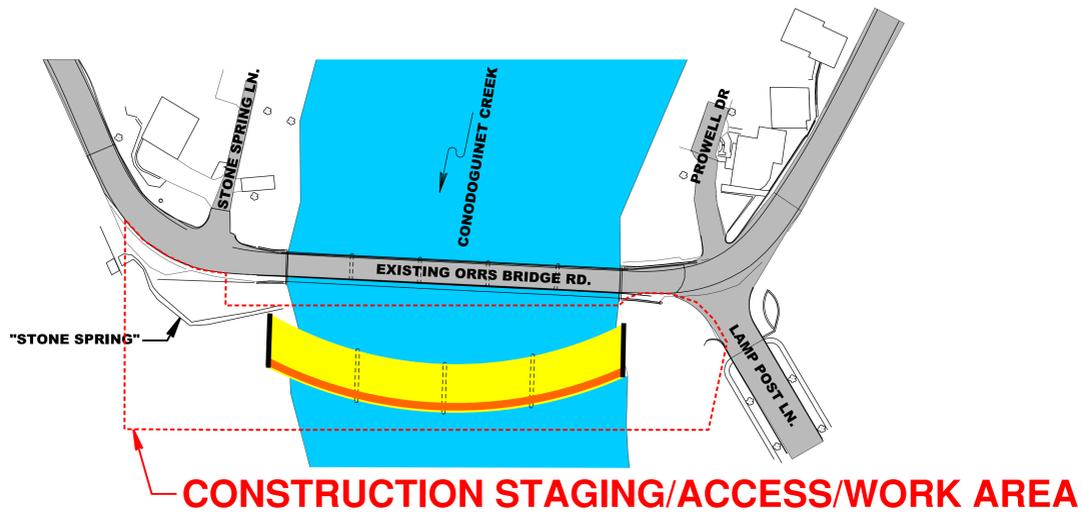


STAGE 1 - CONSTRUCT BRIDGE

- PEDESTRIAN ACCESS TO CROSS BRIDGE AND "STONE SPRING" CLOSED
- MAINTAIN EXISTING TRAFFIC FLOW
- DURATION - APPROX. 7-8 MONTHS

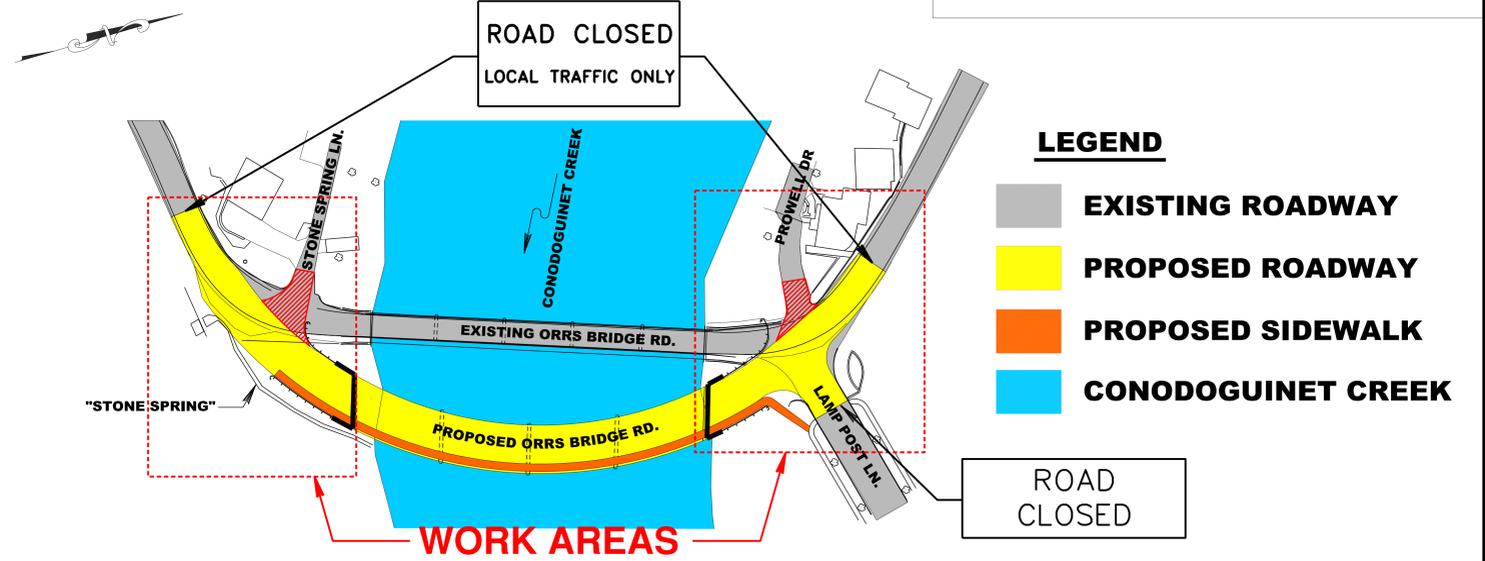


STAGE 2 - CONSTRUCT ROADWAY TIE-IN

- PEDESTRIAN ACCESS TO CROSS BRIDGE AND "STONE SPRING" CLOSED
- DETOUR IMPLEMENTED
- DURATION - APPROX. 3-4 WEEKS

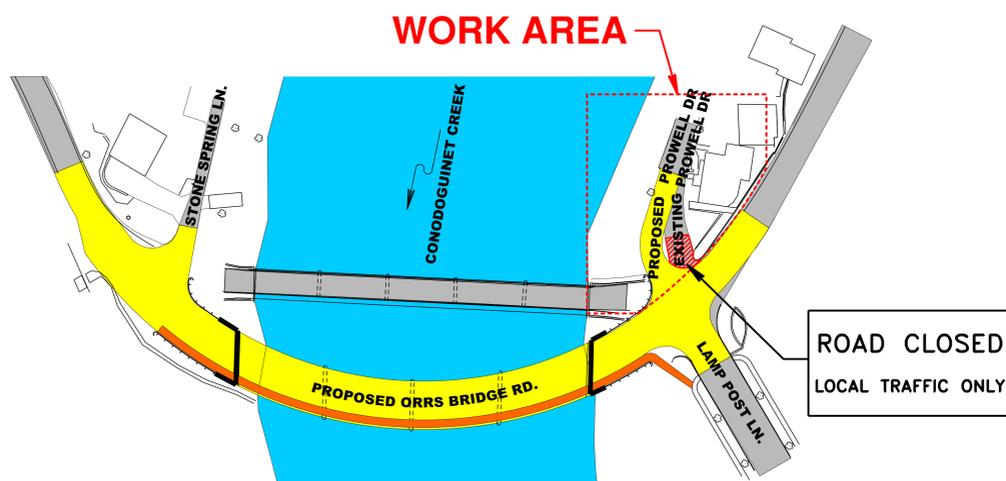

STAGE 3 - RELOCATE PROWELL DRIVE

- PEDESTRIAN ACCESS TO BRIDGE AND "STONE SPRING" OPEN
- TRAFFIC SHIFTED TO NEW BRIDGE
- DURATION - APPROX. 3-5 WEEKS

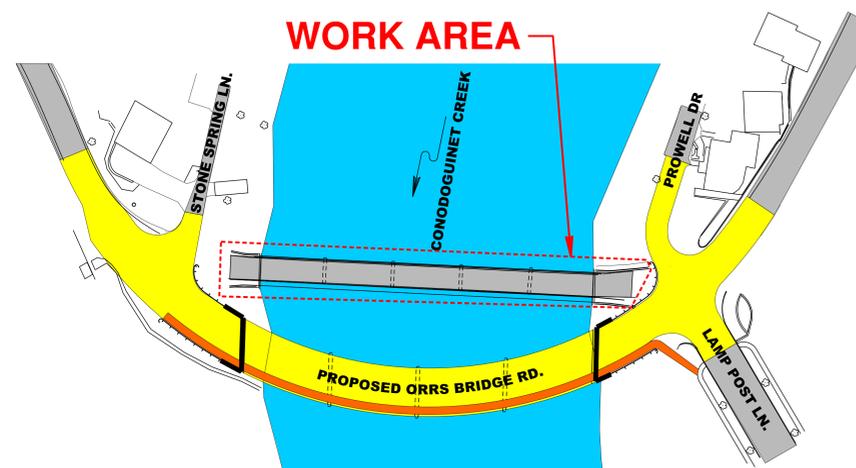

STAGE 4 - DEMOLISH EXISTING BRIDGE

- PEDESTRIAN ACCESS TO BRIDGE AND "STONE SPRING" OPEN
- TRAFFIC UTILIZES NEW BRIDGE
- DURATION - APPROX. 2-3 MONTHS

ORRS BRIDGE REPLACEMENT

HAMPDEN TOWNSHIP - ORRS BRIDGE ROAD
CUMBERLAND COUNTY, PENNSYLVANIA

